


ID	Task Name	Duration	Start	Finish	% Complete	2021				2022				2023				2024			
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	Milestones for Master Schedule (Modesto CH)	4742 days	1/16/12	1/8/25	72%																
2	Site Acquisition Phase	1062 days	1/16/12	12/12/14	100%																
4	Preliminary Plans Phase	885 days	1/13/16	6/15/18	100%																
10	Working Drawings & Approval to Bid	1013 days	8/6/18	5/14/21	100%																
11	Working Drawings & Approval to Bid Summary	1013 days	8/6/18	5/14/21	100%																
12	Working Drawings Notice to Proceed (NTP)	0 days	9/7/18	9/7/18	100%																
13	50% Working Drawings	0 days	2/4/19	2/4/19	100%																
14	90% Working Drawings (Electronic Submittal)	0 days	5/6/19	5/6/19	100%																
15	100% Working Drawings AHJ Submittal Complete	0 days	7/11/19	7/11/19	100%																
16	Authorities Having Jurisdiction (AHJ) Regulatory Review & Approval	0 days	3/24/21	3/24/21	100%																
17	DOF Approval of Working Drawings/Proceed to Bid	0 days	5/14/21	5/14/21	100%																
18	Procurement and Contract Award	108 days	5/15/21	8/30/21	16%																
19	Procurement and Contract Award Summary	108 days	5/15/21	8/30/21	16%																
20	CMR Submit GMP	0 days	7/26/21	7/26/21	0%																
21	DOF Approval - Proceed To Construction	0 days	8/30/21	8/30/21	0%																
22	ARF Transfer/Notice to Proceed	0 days	8/30/21	8/30/21	0%																
23	CMR GMP Contract Amendment	0 days	8/30/21	8/30/21	0%																
24	Construction & Close-out Phase	1096 days	10/11/21	10/10/24	0%																
25	GMP 1	1096 days	10/11/21	10/10/24	0%																
26	Construction Notice to Proceed (NTP)	0 days	10/11/21	10/11/21	0%																
27	Construction Summary	1096 days	10/11/21	10/10/24	0%																
28	Ready For Use	0 days	9/10/24	9/10/24	0%																
29	Construction Finish - Final Completion	0 days	10/10/24	10/10/24	0%																
30	Move-In	30 days	10/10/24	11/9/24	0%																
31	Occupancy Summary	30 days	10/11/24	11/9/24	0%																
32	Start FF&E Installation & Move-In	0 days	10/10/24	10/10/24	0%																
33	Move-in / Occupancy Complete	0 days	11/9/24	11/9/24	0%																
34	Court Opened for Business	0 days	11/9/24	11/9/24	0%																
35	Project Complete	0 days	1/8/25	1/8/25	0%																
36	Warranty Phase	365 days	10/11/24	10/10/25	0%																

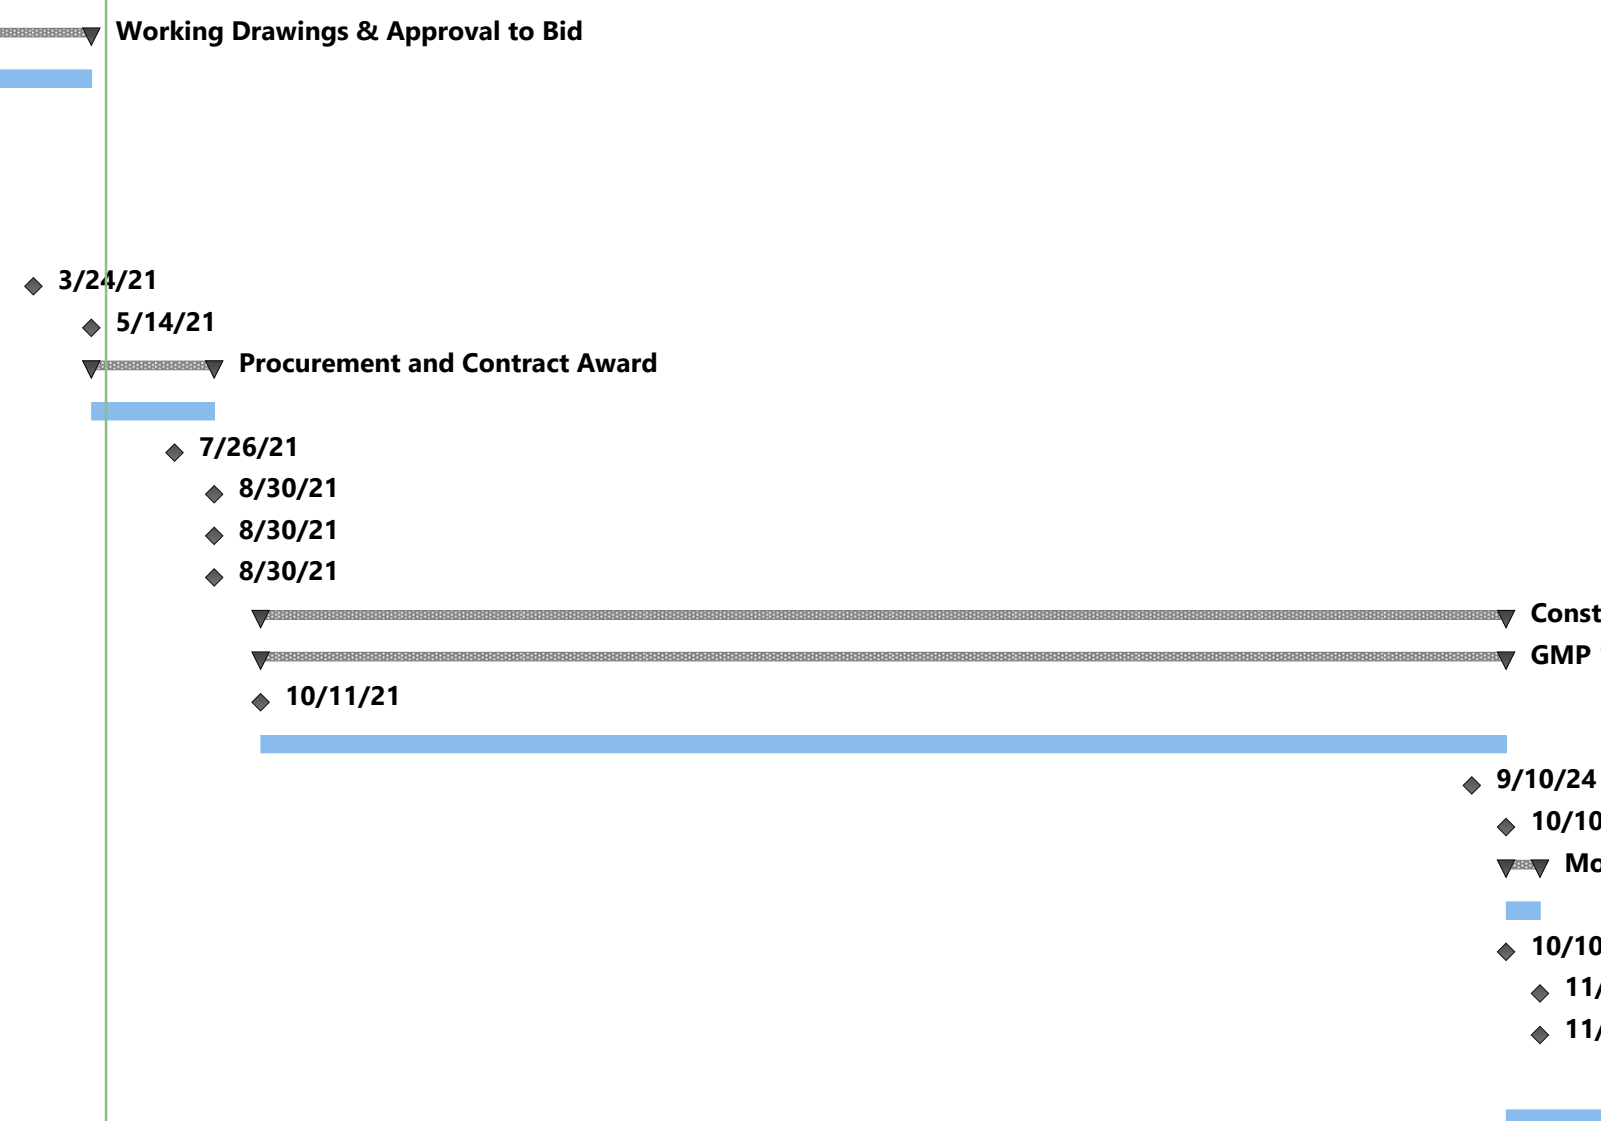

Project: New Modesto Courthouse
Date: 5/28/21


Task Milestone Summary Manual Task

ID	Task Name	Duration	Start	Finish	% Complete	2021				2022				2023				2024				
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
37	JCC - New Modesto Courthouse Project	4941 days	7/1/11	1/8/25	67%																	
38	New Judgeship Process - JCC/DOF	180 days	4/1/15	12/8/15	100%																	
39	PWB/DOF approval of new judgeship	0 days	12/8/15	12/8/15	100%																	
40	Consultant Agreements	2667 days	7/1/11	10/18/18	100%																	
80	Site Acquisition	751 days	1/16/12	12/1/14	100%																	
81	Preliminary Plan Phase	902 days	1/13/16	7/2/18	100%																	
218	Working Drawing Phase	1047 days	7/2/18	5/14/21	100%																	
219	Funding Authorization for WD (Form 14D)	15 days	7/3/18	7/17/18	100%																	
220	Approval of State Budget FY 18-19	0 days	7/2/18	7/2/18	100%																	
221	Amendments to Agreements	67 days	7/3/18	9/7/18	100%																	
222	Construction Documents	1012 days	8/7/18	5/14/21	100%																	
223	CD Tasks	456 days	8/7/18	11/5/19	100%																	
248	Authorities Having Jurisdiction (AHJ) Review	585 days	10/8/19	5/14/21	100%																	
249	BSCC Review	60 days	11/6/19	1/4/20	100%																	
250	DSA Review	60 days	11/6/19	1/4/20	100%																	
251	SFM Initial Review	120 days	10/8/19	2/4/20	100%																	
252	Incorporate AHJ Comments	27 days	2/5/20	3/2/20	100%																	
253	SFM Back Check #1	28 days	3/3/20	3/30/20	100%																	
254	Incorporate AHJ Comments #1	10 days	3/31/20	4/9/20	100%																	
255	SFM Back Check #2	11 days	4/10/20	4/20/20	100%																	
256	BSCC Back check and Approval	21 days	3/31/20	4/20/20	100%																	
257	DSA Back check and Approval	20 days	3/31/20	4/19/20	100%																	
258	SFM Back check #3	137 days	3/31/20	8/14/20	100%																	
259	Incorporate AHJ Comments #3	32 days	8/15/20	9/15/20	100%																	
260	SFM Back check #4 (Approval)	190 days	9/16/20	3/24/21	100%																	
261	AHJ Review & Approval	0 days	3/24/21	3/24/21	100%																	
262	DOF review	50 days	3/25/21	5/13/21	100%																	
263	DOF Authorization to Bid	1 day	5/14/21	5/14/21	100%																	
264	DOF Approval of Working Drawings/Proceed to Bid	0 days	5/14/21	5/14/21	100%																	
265	Procurement Phase - Bid and Award	108 days	5/15/21	8/30/21	5%																	
266	CMR Bid Trades - Advertise / Solicit Bids	45 days	5/15/21	6/28/21	38%																	
267	Conduct Pre-bid DVBE Meeting	1 day	5/20/21	5/20/21	100%																	
268	CMR Prepare GMP	28 days	6/29/21	7/26/21	0%																	
269	CMR Submit GMP	0 days	7/26/21	7/26/21	0%																	
270	GMP Negotiation (Scope Review Meetings)	7 days	7/27/21	8/2/21	0%																	
271	Establish GMP	14 days	8/3/21	8/16/21	0%																	
272	Write & compile submittal to DOF	14 days	8/3/21	8/16/21	0%																	
273	DOF/JCC approval of GMP	14 days	8/17/21	8/30/21	0%																	
274	DOF Approval - Proceed To Construction	0 days	8/30/21	8/30/21	0%																	
275	Amendments to Agreements / ARF Transfer/Notice to Proce	60 days	7/2/21	8/30/21	0%																	
276	CMA Contract Amendment	35 days	7/27/21	8/30/21	0%																	

Project: New Modesto Courtho Date: 5/28/21

Task ■ Milestone ◆ Summary ▬ Manual Task ■

ID	Task Name	Duration	Start	Finish	% Complete	2021				2022				2023				2024			
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
277	IOR Contract Amendment	35 days	7/27/21	8/30/21	0%																
278	CMR Contract Amendment	35 days	7/27/21	8/30/21	0%																
279	A/E Contract Amendment (Construction)	60 days	7/2/21	8/30/21	0%																
280	CMR GMP Contract Amendment	0 days	8/30/21	8/30/21	0%																
281	Construction & Close-out Phase	1097 days	10/10/21	10/10/24	0%																
282	Construction Notice to Proceed (NTP)	0 days	10/11/21	10/11/21	0%																
283	Construction Administration	1097 days	10/10/21	10/10/24	0%																
284	Construction	1097 days	10/10/21	10/10/24	0%																
285	Substructure Complete	0 days	7/11/22	7/11/22	0%																
286	Structural Steel Complete	0 days	10/28/22	10/28/22	0%																
287	Building Dry-In	0 days	4/11/23	4/11/23	0%																
288	Exterior Complete	0 days	9/23/23	9/23/23	0%																
289	Ready For Use	0 days	9/10/24	9/10/24	0%																
290	Converged Network Integration	78 days	6/25/24	9/10/24	0%																
291	Commissioning	120 days	5/14/24	9/10/24	0%																
292	Punchlist Completion	30 days	9/11/24	10/10/24	0%																
293	Construction Finish - Final Completion (Projected)	0 days	10/10/24	10/10/24	0%																
294	Construction Finish - Final Completion (Contractual)	0 days	10/10/24	10/10/24	0%																
295	JCC Move-In / Activation	30 days	10/10/24	11/9/24	0%																
296	Start FF&E Installation& Move-In	0 days	10/10/24	10/10/24	0%																
297	FF&E Installation	30 days	10/11/24	11/9/24	0%																
298	Move-in and Occupancy (JCC)	30 days	10/11/24	11/9/24	0%																
299	Staff Training	30 days	10/11/24	11/9/24	0%																
300	Move-in / Occupancy Complete	0 days	11/9/24	11/9/24	0%																
301	Contract Close-out	90 days	10/11/24	1/8/25	0%																
302	LEED Certification	83 days	10/11/24	1/1/25	0%																
303	Close Contracts	90 days	10/11/24	1/8/25	0%																
304	Archive Record Documents	61 days	10/11/24	12/10/24	0%																
305	Court Opened for Business	0 days	11/9/24	11/9/24	0%																
306	Project Complete	0 days	1/8/25	1/8/25	0%																

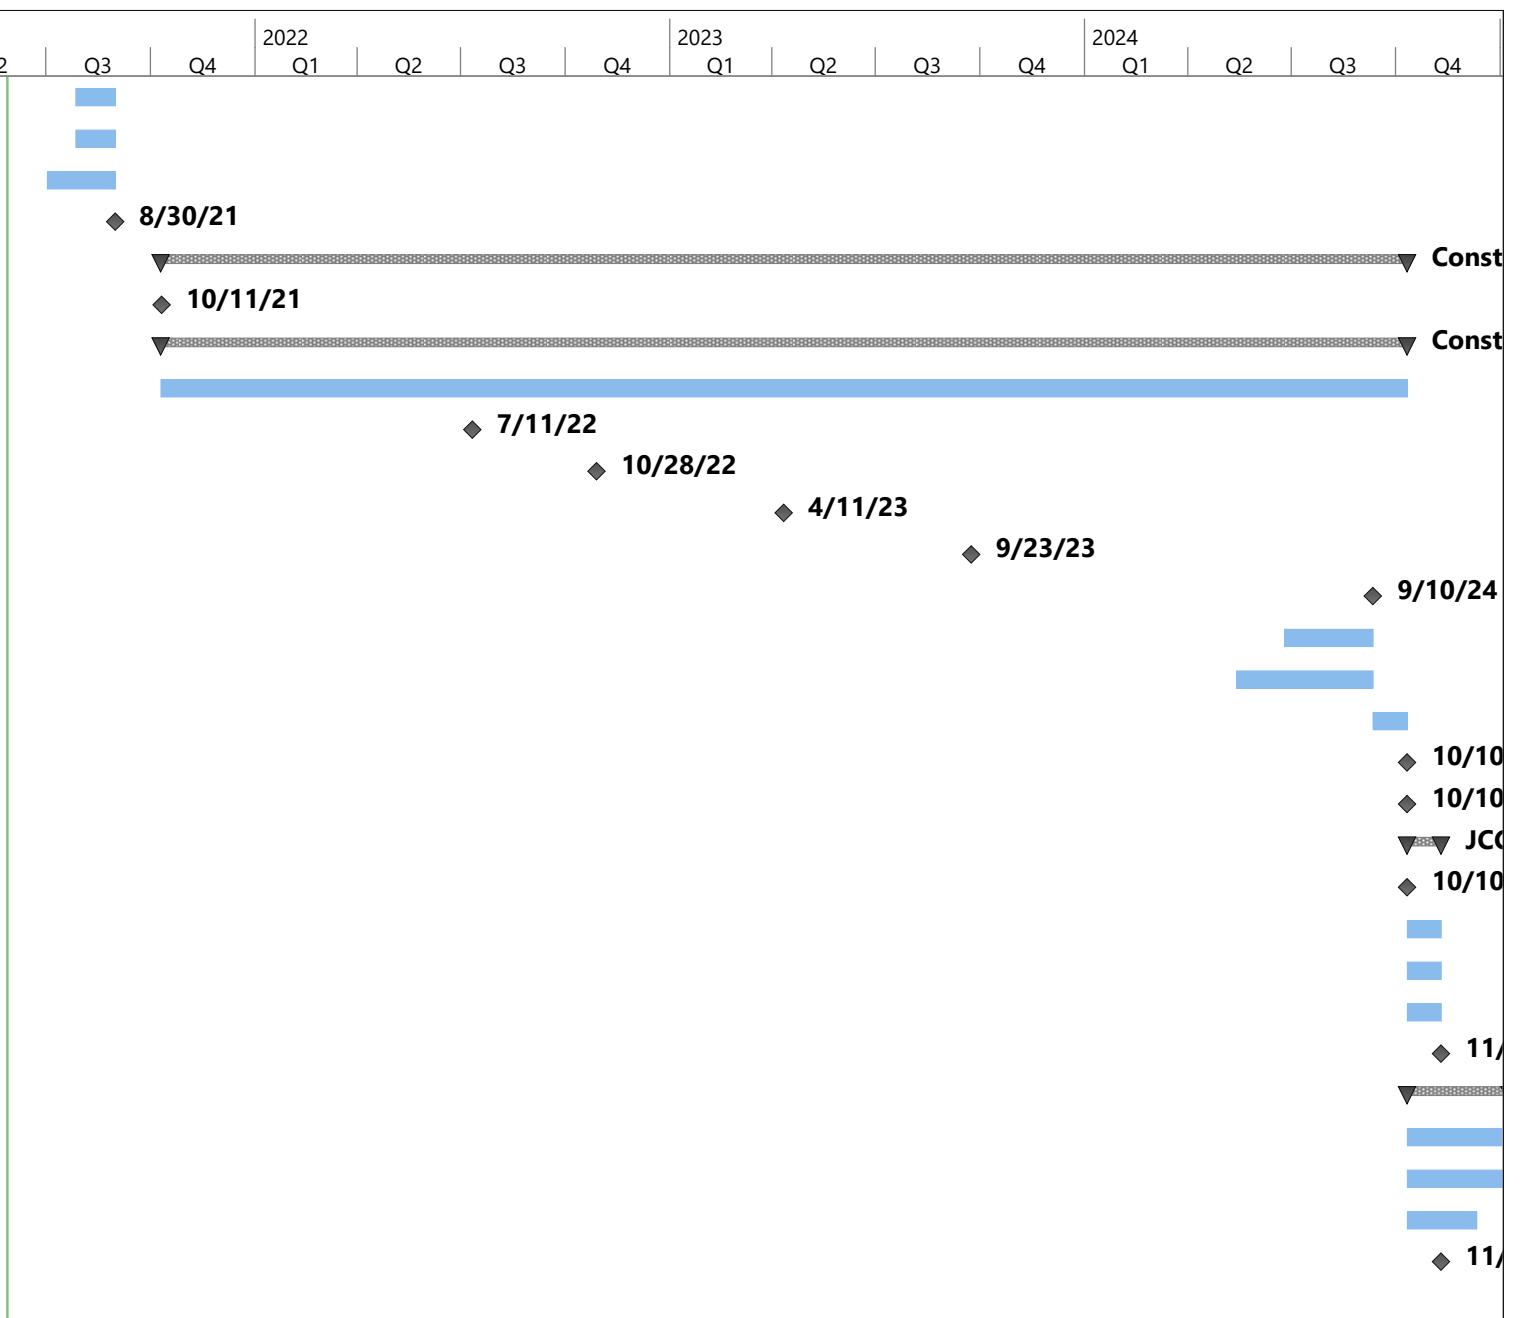

Project: New Modesto Courtho
Date: 5/28/21

Task Milestone Summary Manual Task
